


Project: JUPITER INLET LIGHTHOUS Date: Mon 5/17/21	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	


ID	Task Name	Duration	Start	Finish	May 2, '21			May 30, '21		Jun 27, '21		Jul 25, '21		Aug 22, '21		Sep 19, '21		Oct 17, '21			Nov 14, '21		Dec 12, '21		Jan 9, '22		Feb 6, '22	
					W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S
37	External Sheathing	8 days	Tue 8/24/21	Thu 9/2/21																								
38	Gypsum Board Soffits	8 days	Tue 8/24/21	Thu 9/2/21																								
39	Thermal & Moisture Protection	12 days	Tue 8/31/21	Wed 9/15/21																								
40	Thermal Insulation	10 days	Tue 8/31/21	Mon 9/13/21																								
41	Roof Treatment	6 days	Tue 9/7/21	Tue 9/14/21																								
42	Sealants	5 days	Thu 9/9/21	Wed 9/15/21																								
43	Metal Work	19 days	Fri 9/3/21	Wed 9/29/21																								
44	Metal Gutters	6 days	Fri 9/3/21	Fri 9/10/21																								
45	Hand Railing	4 days	Fri 9/10/21	Wed 9/15/21																								
46	Other Metal Fabrication	10 days	Thu 9/16/21	Wed 9/29/21																								
47	Openings	10 days	Thu 9/16/21	Wed 9/29/21																								
48	Hollow Metal Doors & Frames	10 days	Thu 9/16/21	Wed 9/29/21																								
49	Aluminium Windows	10 days	Thu 9/16/21	Wed 9/29/21																								
50	Door Hardwares	4 days	Fri 9/24/21	Wed 9/29/21																								
51	Finishing	38 days	Fri 9/24/21	Tue 11/16/21																								
52	Asphalt Shingle Roofing	10 days	Fri 9/24/21	Thu 10/7/21																								
53	Gypsum Wall Board	8 days	Fri 10/1/21	Tue 10/12/21																								
54	Wall Plastering	10 days	Thu 10/7/21	Wed 10/20/21																								
55	Interior Painting	14 days	Wed 10/13/21	Mon 11/1/21																								
56	Exterior Stucco Finish	9 days	Thu 10/21/21	Tue 11/2/21																								
57	Suspended Ceiling	10 days	Mon 10/25/21	Fri 11/5/21																								
58	Resinous Flooring	10 days	Fri 10/29/21	Thu 11/11/21																								
59	Water Resistant Tile Flooring	7 days	Mon 11/8/21	Tue 11/16/21																								
60	Plumbing Work	75 days	Tue 8/10/21	Mon 11/22/21																								
61	Piping & Fittings	70 days	Tue 8/10/21	Mon 11/15/21																								
62	Installation of W.Cs	5 days	Tue 11/16/21	Mon 11/22/21																								
63	Installation of Sinks	5 days	Tue 11/16/21	Mon 11/22/21																								
64	Provision of Vent Piping	4 days	Wed 11/17/21	Mon 11/22/21																								
65	Installation of Water Heaters	2 days	Fri 11/19/21	Mon 11/22/21																								
66	Electrcal Work	87 days	Mon 8/9/21	Tue 12/7/21																								
67	Conduiting & Wiring	73 days	Mon 8/9/21	Wed 11/17/21																								
68	Sockets & Outlets	10 days	Thu 11/4/21	Wed 11/17/21																								
69	Distribution System	7 days	Thu 11/11/21	Fri 11/19/21																								
70	Switches & Circuit Breakers	5 days	Wed 11/17/21	Tue 11/23/21																								
71	Lighting Fixtures	15 days	Wed 11/17/21	Tue 12/7/21																								
72	Emergancy & Exit Lightings	4 days	Thu 12/2/21	Tue 12/7/21																								
73	HVAC Work	19 days	Wed 11/17/21	Mon 12/13/21																								
74	Ducting	15 days	Wed 11/17/21	Tue 12/7/21																								
75	Air Filtering System	6 days	Thu 12/2/21	Thu 12/9/21																								
76	Refrigerators & Grills	6 days	Thu 12/2/21	Thu 12/9/21																								
77	Split Air Conditioning System	6 days	Mon 12/6/21	Mon 12/13/21																								
78	Specialities & Equipments	12 days	Wed 11/17/21	Thu 12/2/21																								
79	Cabinets & Counter Tops	10 days	Wed 11/17/21	Tue 11/30/21																								
80	Washroom Accessories	6 days	Thu 11/25/21	Thu 12/2/21																								

Watermark: Consultants

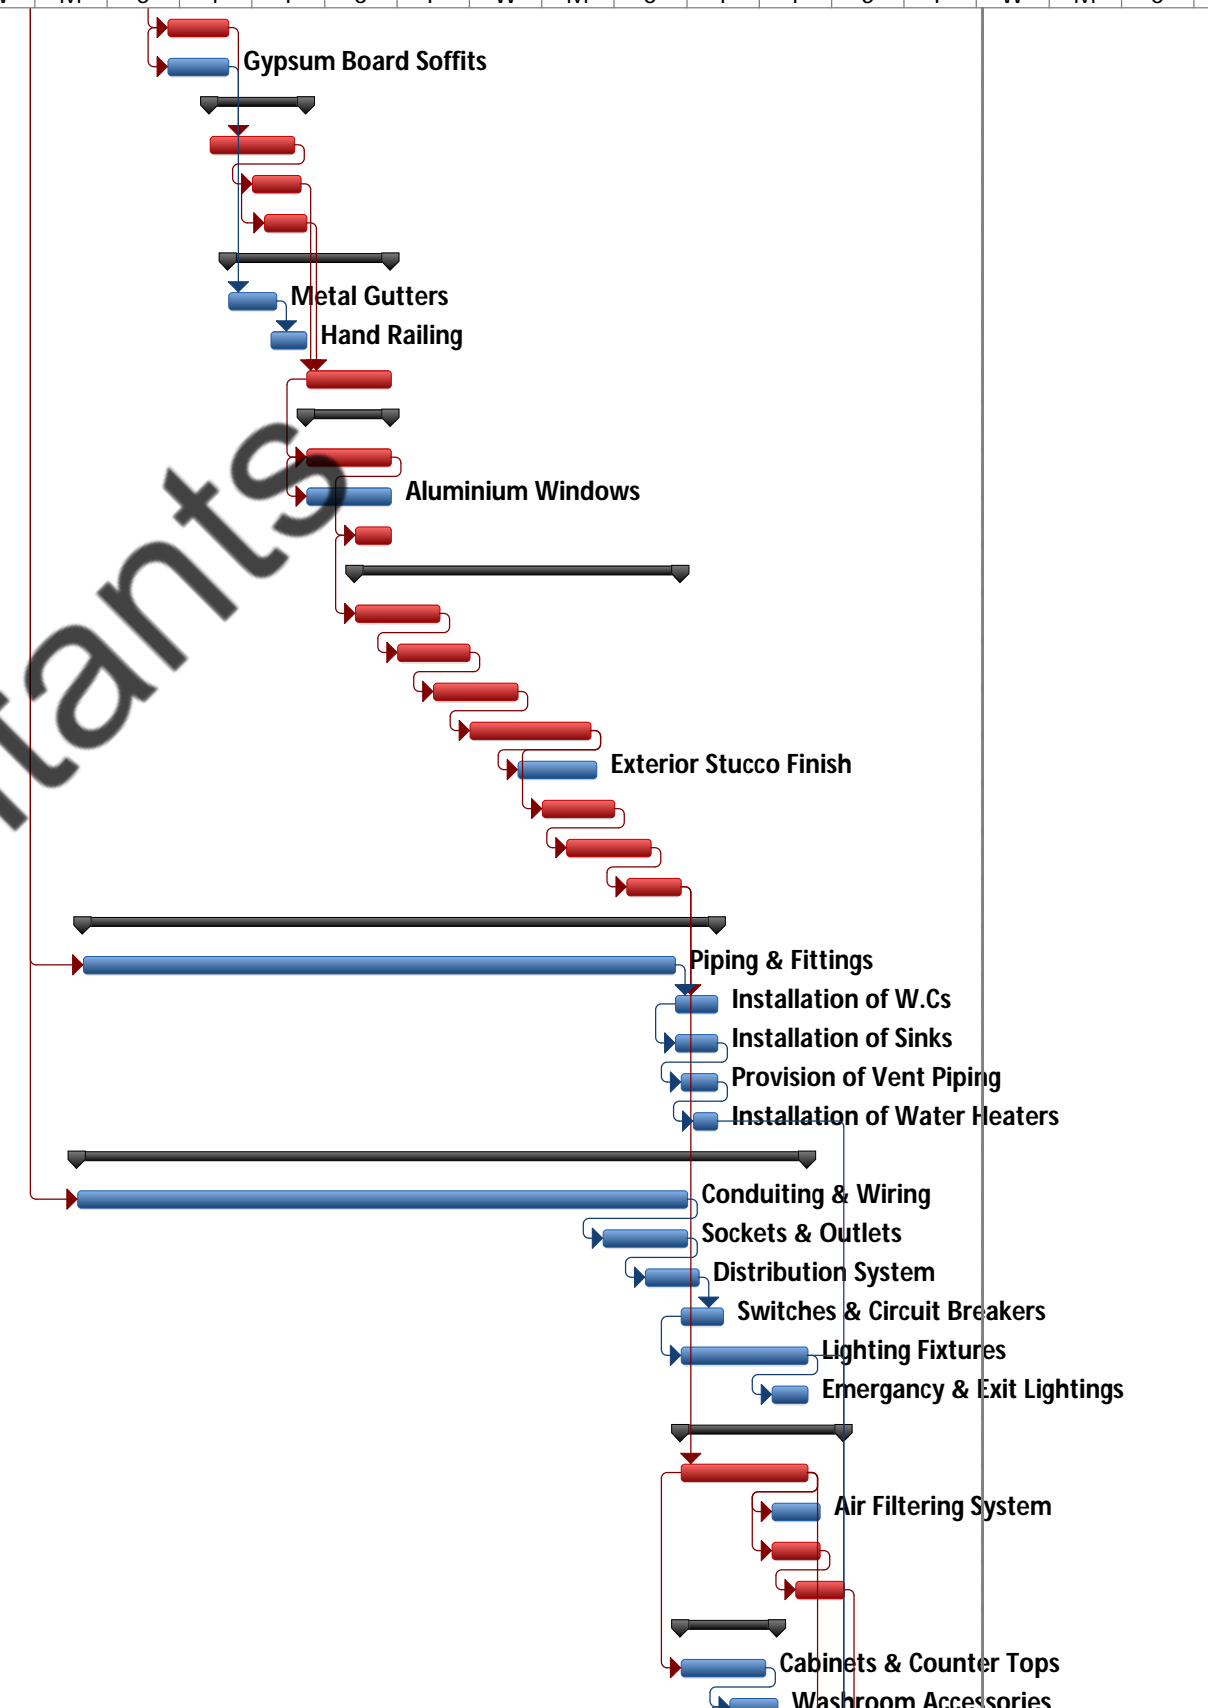

Project: JUPITER INLET LIGHTHOUSE Date: Mon 5/17/21	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

ID	Task Name	Duration	Start	Finish	May 2, '21		May 30, '21		Jun 27, '21		Jul 25, '21		Aug 22, '21		Sep 19, '21		Oct 17, '21		Nov 14, '21		Dec 12, '21		Jan 9, '22		Feb 6, '22	
					W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S	T	T	S	F	W
81	Utility Equipments	6 days	Thu 11/25/21	Thu 12/2/21																						
82	Fire Extinguishers	2 days	Wed 12/1/21	Thu 12/2/21																						
83	External Work	8 days	Wed 12/8/21	Fri 12/17/21																						
84	Concrete Paving	7 days	Wed 12/8/21	Thu 12/16/21																						
85	External Repairing & Rectification	4 days	Tue 12/14/21	Fri 12/17/21																						
86	Closeout	17 days	Tue 12/14/21	Wed 1/5/22																						
87	Testing & Commissioning	12 days	Tue 12/14/21	Wed 12/29/21																						
88	Final Cleanout	7 days	Thu 12/23/21	Fri 12/31/21																						
89	Final Inspection	5 days	Wed 12/29/21	Tue 1/4/22																						
90	Final Sign-Off	3 days	Mon 1/3/22	Wed 1/5/22																						
91	Final Completion	0 days	Wed 1/5/22	Wed 1/5/22																						

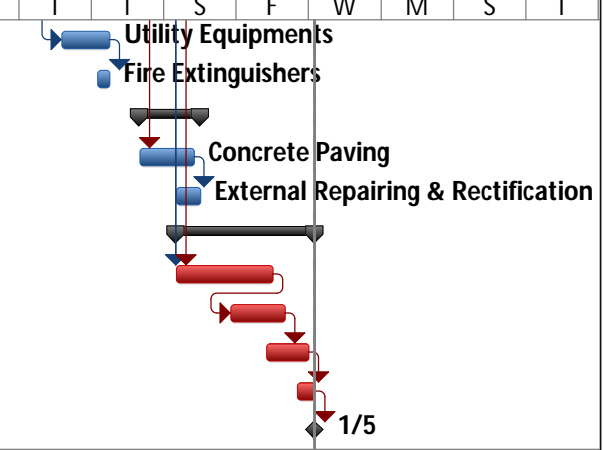

VTI Consultants

Project: JUPITER INLET LIGHTHOUSE Date: Mon 5/17/21	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	
